

CVR & EPC KPI'S



CVR / EPC Current Bids

In Progress

Due Now

Due within one week

Bid Due Date	Customer	Job Name	Job Description	Group
5/27/2026	DTE Energy	Renaissance 345kV Substation	Replacement of six 345kV MOD switches - ON HOLD	CVR


Pending

Bid Due Date	Customer	Job Name	Job Description	Job Value	Group
12/23/2025	Steuben County REMC	Frontier Make Ready	10 packages of make ready evaluation.	\$100,000	CVR
2/4/2026	Hoosier Energy R.E.C., INC	Jacksonburg to Gateway	New 69kV line, 2.2miles, EPC to connect Jacksonburg Substation to Gateway Substation. Three-way switch at each end, design to be wood-equivalent and guying. Include space for future under-build.	\$160,000	CVR
				\$3,548,538	EPC
2/13/2026	Hoosier Energy R.E.C., INC	Rosehill to Rockport	New 69kV line, 3.8miles, EPC to connect Rosehill Substation to Rockport Line Switch. Three-way switch at each end, design to be wood-equivalent and guying. Include space for future under-build.	\$290,000	CVR
				\$5,590,941	EPC
5/27/2026	Lansing Board of Water & Light	Joint Use Audit	Joint use audit.	\$1,350,000	CVR
6/26/2026	Consumers Energy	2026 Pole Replacements	Replacement of 168 Poles	\$276,450	CVR
				\$3,451,137	EPC


Awarded

Award Date	Customer	Job Name	Job Description	Job Value	Group
------------	----------	----------	-----------------	-----------	-------

2025 CVR Win/Loss Rate



2026 CVR Win/Loss Rate



CVR Project Scorecard

 PM:
 Week Ending:

Roy Pierce	
7/11/2026	

Project ID/Job #	001-0001	Job Title	DTE - Catalina Conversion Phase 3		
Description	Design & engineering associated with 5.7 miles of 8.3kV to 13.2kV conversion of Catalina circuits				
Start Date	10/17/2023	Finish Date	6/27/2025	% Complete	100%
PO Value	\$838,451	Est. Finish Costs	\$495,492	Cost% +/-	40.9%
Work In Progress	Construction Support			Plan Margin	32.7%
Open Issues				Total Billed	\$806,331

Project ID/Job #	001-0003	Job Title	DTE - New Baltimore Conversion		
Description	Design & engineering associated with 4.8kV to 13.2kV conversion of New Baltimore circuits				
Start Date	6/20/2025	Finish Date	12/30/2027	% Complete	64%
PO Value	\$1,428,796	Est. Finish Costs	\$512,077	Cost% +/-	64.2%
Work In Progress	Construction Support.			Plan Margin	65.8%
Open Issues				Total Billed	\$1,216,312

Project ID/Job #	005-0004	Job Title	Consumers Energy - 2026 HVD Line Sensors		
Description	HVD & LVD BOM Development				
Start Date	5/11/2026	Finish Date	10/31/2026	% Complete	77%
PO Value	\$130,493	Est. Finish Costs	\$67,353	Cost% +/-	48.4%
Work In Progress	Development of Record Prints.			Plan Margin	32.2%
Open Issues				Total Billed	\$71,268

Project ID/Job #	016-0001	Job Title	Cloverland - Manistique Pump Station		
Description	New 69/4.1kV substation adjacent to existing station				
Start Date	6/5/2024	Finish Date	9/30/2026	% Complete	99%
PO Value	\$111,510	Est. Finish Costs	\$341,637	Cost% +/-	-206.4%
Work In Progress				Plan Margin	19.4%
Open Issues	Awaiting Record Prints.			Total Billed	\$106,628

Project ID/Job #	017-0001	Job Title	Centerpoint - Winslow 69kV Substation		
Description	Replace 69kV breakers and disconnects and associated relays				
Start Date	2/24/2025	Finish Date	8/1/2026	% Complete	100%
PO Value	\$105,801	Est. Finish Costs	\$203,587	Cost% +/-	-92.4%
Work In Progress				Plan Margin	34.9%
Open Issues				Total Billed	\$105,791

Project ID/Job #	017-0002	Job Title	Centerpoint - Pigeon Creek 69kV Substation		
Description	Install new 69kV fuseless Cap Bank w/reactor, 69kV breaker and switches. Upgrade cap bank protection and control.				
Start Date	11/14/2025	Finish Date	5/15/2026	% Complete	99%
PO Value	\$102,016	Est. Finish Costs	\$79,466	Cost% +/-	22.1%
Work In Progress				Plan Margin	42.2%
Open Issues	Awaiting Record Prints.			Total Billed	\$102,011

Project ID/Job #	017-0003	Job Title	Centerpoint - Gateway 69kV Substation		
Description	Add 69kV Breakers and Protection				
Start Date	12/10/2025	Finish Date	8/6/2026	% Complete	65%
PO Value	\$203,015	Est. Finish Costs	\$135,463	Cost% +/-	33.3%
Work In Progress	90% Submittal			Plan Margin	42.3%
Open Issues				Total Billed	\$131,230

Project ID/Job #	017-0004	Job Title	Centerpoint - Rockport 69kV Substation		
Description	Replace Existing 69kV Line and Breaker Relaying				
Start Date	12/10/2025	Finish Date	8/6/2026	% Complete	88%
PO Value	\$96,712	Est. Finish Costs	\$65,395	Cost% +/-	32.4%
Work In Progress	IFC Submittal			Plan Margin	40.2%
Open Issues				Total Billed	\$81,692

Project ID/Job #	017-0005	Job Title	Centerpoint - Angel Mounds 69kV Substation		
Description	Install New 69kV Cap Bank				
Start Date	12/10/2025	Finish Date	10/28/2026	% Complete	88%
PO Value	\$96,987	Est. Finish Costs	\$89,396	Cost% +/-	7.8%
Work In Progress	90% Submittal			Plan Margin	42.8%
Open Issues				Total Billed	\$95,148

Project ID/Job #	017-0006	Job Title	Centerpoint - Northwest 69kV Substation		
Description	Install two new 69kV capacitor banks				
Start Date	6/9/2026	Finish Date	8/6/2027	% Complete	13%
PO Value	\$110,555	Est. Finish Costs	\$60,191	Cost% +/-	45.6%
Work In Progress	Awaiting 30% Comments and Kickoff			Plan Margin	36.2%
Open Issues				Total Billed	\$4,365

Project ID/Job #	017-0007	Job Title	Centerpoint - Leonard Rd 69kV Substation		
Description	Install two new 69kV capacitor banks and converting to breaker and a half				
Start Date	6/9/2026	Finish Date	10/28/2027	% Complete	17%
PO Value	\$199,994	Est. Finish Costs	\$104,744	Cost% +/-	47.6%
Work In Progress	30% Submittal and kickoff			Plan Margin	38.6%
Open Issues				Total Billed	\$6,739

Project ID/Job #	022-0001	Job Title	Ambor - Galaxy Tline		
Description	Structural Analysis Review				
Start Date	2/27/2026	Finish Date	3/31/2026	% Complete	100%
PO Value	\$5,200	Est. Finish Costs	\$3,086	Cost% +/-	40.7%
Work In Progress				Plan Margin	43.9%
Open Issues				Total Billed	\$5,200

EPC Project Scorecard

PM:

Ethan McDaniel

Week Ending:

7/11/2026

Project ID/Job #	24000168	Job Title	MEC/Sub P GSU & Substation		
Description	Sub upgrades - GSU section (above & below grade) & Substation section (below grade)				
Start Date	7/16/2024	Finish Date	10/31/2026	% Complete	83%
PO Value	\$6,579,649	Est Finish Cost	\$7,849,644	Cost% +/-	-19.3%
Work In Progress	Engineering: IFCs for Phase 2 submitted.			Plan Margin	16.4%
	Procurement: All outage material received.				
Open Issues	Construction: Outage June 1.			Total Billed	\$5,767,694
	Cost +/- breakdown: 6.9% profit, 3.9% risk contingency				

Project ID/Job #	24000170	Job Title	MEC/Enterprise Way South Substation		
Description	Greenfield 161kV substation installation				
Start Date	9/4/2024	Finish Date	4/17/2026	% Complete	99.6%
PO Value	\$6,335,471	Est Finish Cost	\$6,109,019	Cost% +/-	3.6%
Work In Progress	Engineering: Waiting for as built from Mid-American			Plan Margin	14.6%
	Procurement: Long lead MEC backfill.				
Open Issues	Construction: Substantially complete. Received final punch list.			Total Billed	\$6,314,831
	Cost +/- breakdown: 11.8% profit, 2.8% risk contingency				

Project ID/Job #	24000188	Job Title	MEC/SE Soteria Substation		
Description	161kV Substation Expansion - Phase III, IV, & V				
Start Date	7/16/2024	Finish Date	8/26/2025	% Complete	100%
PO Value	\$4,470,474	Est Finish Cost	\$4,956,902	Cost% +/-	-10.9%
Work In Progress	Engineering: Substantially complete, ongoing construction support as needed.			Plan Margin	14.4%
	Procurement: Substantially complete, ongoing construction support as needed.				
Open Issues	Construction: Phase 4 energized, MEC Sub Ops began phase 5.			Total Billed	\$4,468,681
	Cost +/- breakdown: 8.7% profit, 1.8% risk contingency				

Project ID/Job #	24000189	Job Title	MEC/Johnson Creek Substation		
Description	161kV Substation Expansion - Phase III, IV, & V				
Start Date	7/16/2024	Finish Date	10/7/2025	% Complete	100%
PO Value	\$4,324,547	Est Finish Cost	\$4,938,493	Cost% +/-	-14.2%
Work In Progress	Engineering: Substantially completed, ongoing construction support.			Plan Margin	12.7%
	Procurement: Ongoing material support from Olsson.				
Open Issues	Construction: Phase 4 energized, MEC Sub Ops advised that phase 5 to start soon.			Total Billed	\$4,324,547
	Cost +/- breakdown: 10.9% profit, 1.7% risk contingency				



CVR Outstanding Accounts Receivables

Internal Reference 	Adjustment To	Certificate Reference 	Customer Name 	Job 	Ph	Series 	Txn 	Certificate Date 	Due Date 	Retention	Certified Payment	Balance	Currency	Status
042600001		021-0001-001	GREAT LAKES ENERGY	021-0001		Detail	001	04/20/26	05/20/26	0.00	13,376.61	13,376.61	USD	Unpaid
062600001		017-0005-006	CENTERPOINT ENERGY	017-0005		Detail	006	06/22/26	08/21/26	0.00	8,219.34	8,219.34	USD	Unpaid
062600002		017-0004-006	CENTERPOINT ENERGY	017-0004		Detail	006	06/22/26	08/21/26	0.00	16,746.97	16,746.97	USD	Unpaid
062600003		017-0003-006	CENTERPOINT ENERGY	017-0003		Detail	006	06/22/26	08/21/26	0.00	17,021.46	17,021.46	USD	Unpaid
062600004		017-0006-001	CENTERPOINT ENERGY	017-0006		Detail	001	06/23/26	08/07/26	0.00	4,365.39	4,365.39	USD	Unpaid
062600005		017-0007-001	CENTERPOINT ENERGY	017-0007		Detail	001	06/23/26	08/07/26	0.00	6,738.73	6,738.73	USD	Unpaid




2026 Hours Utilization


Total Billable Utilization vs Median Target Billable Utilization

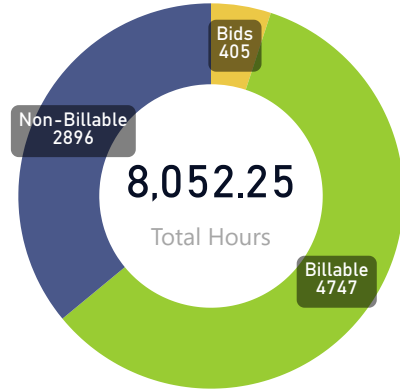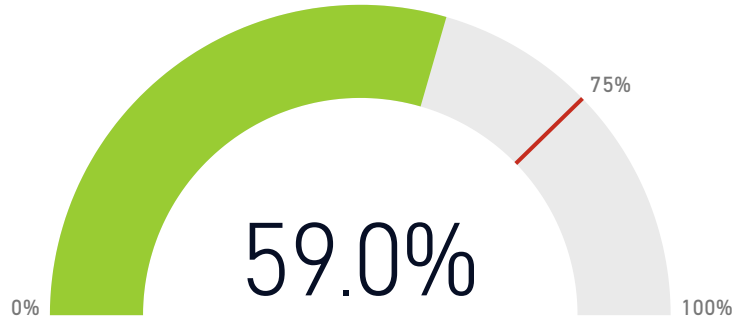


Billable Utilization vs Target Billable Utilization by Employee

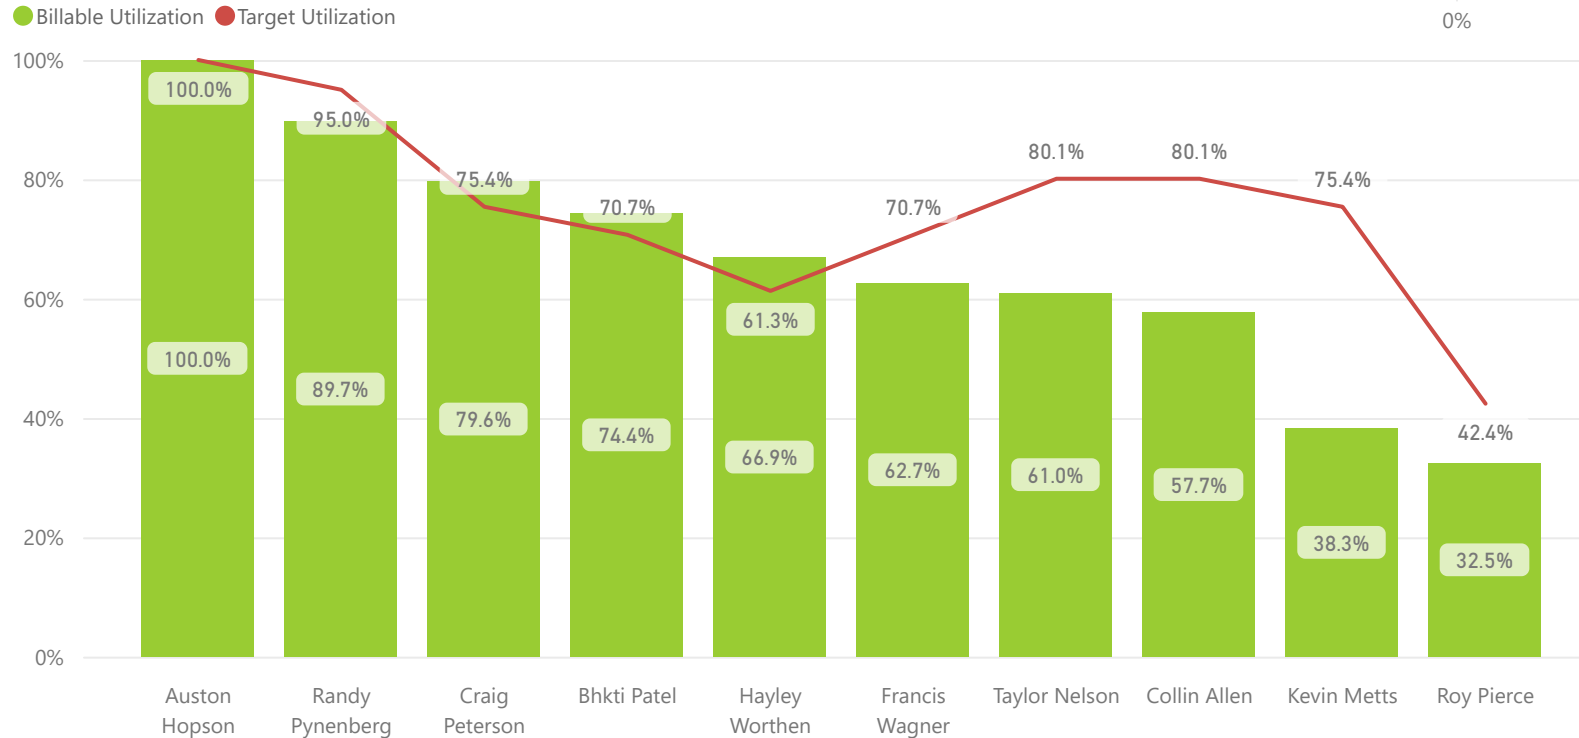

Hours Utilization by Employee

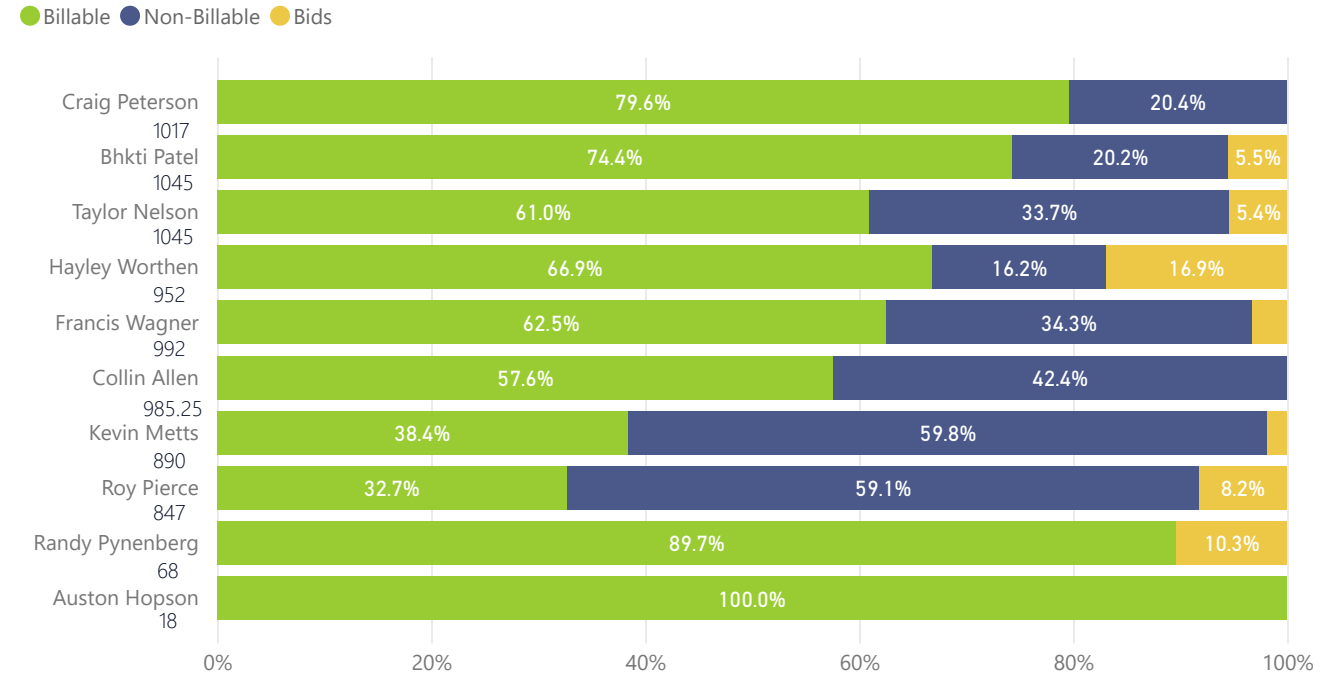

Design Hours by WorkType

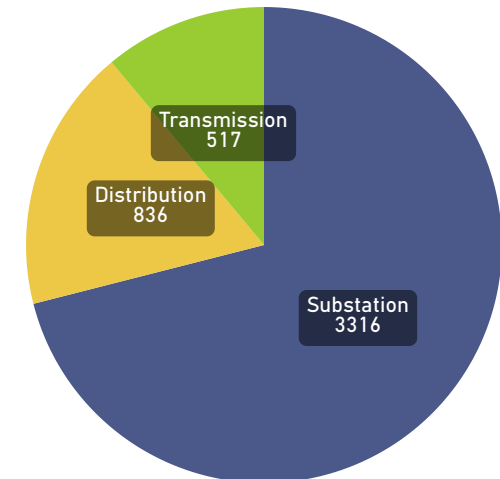



Hours Utilization by Customer

182

Total Business Development
Hours

408


Total Proposal Development
Hours

20%


Bids & Business Development
% of Non-Billable Hours

Development Hours by Customer

● Business Development Hours ● Bids

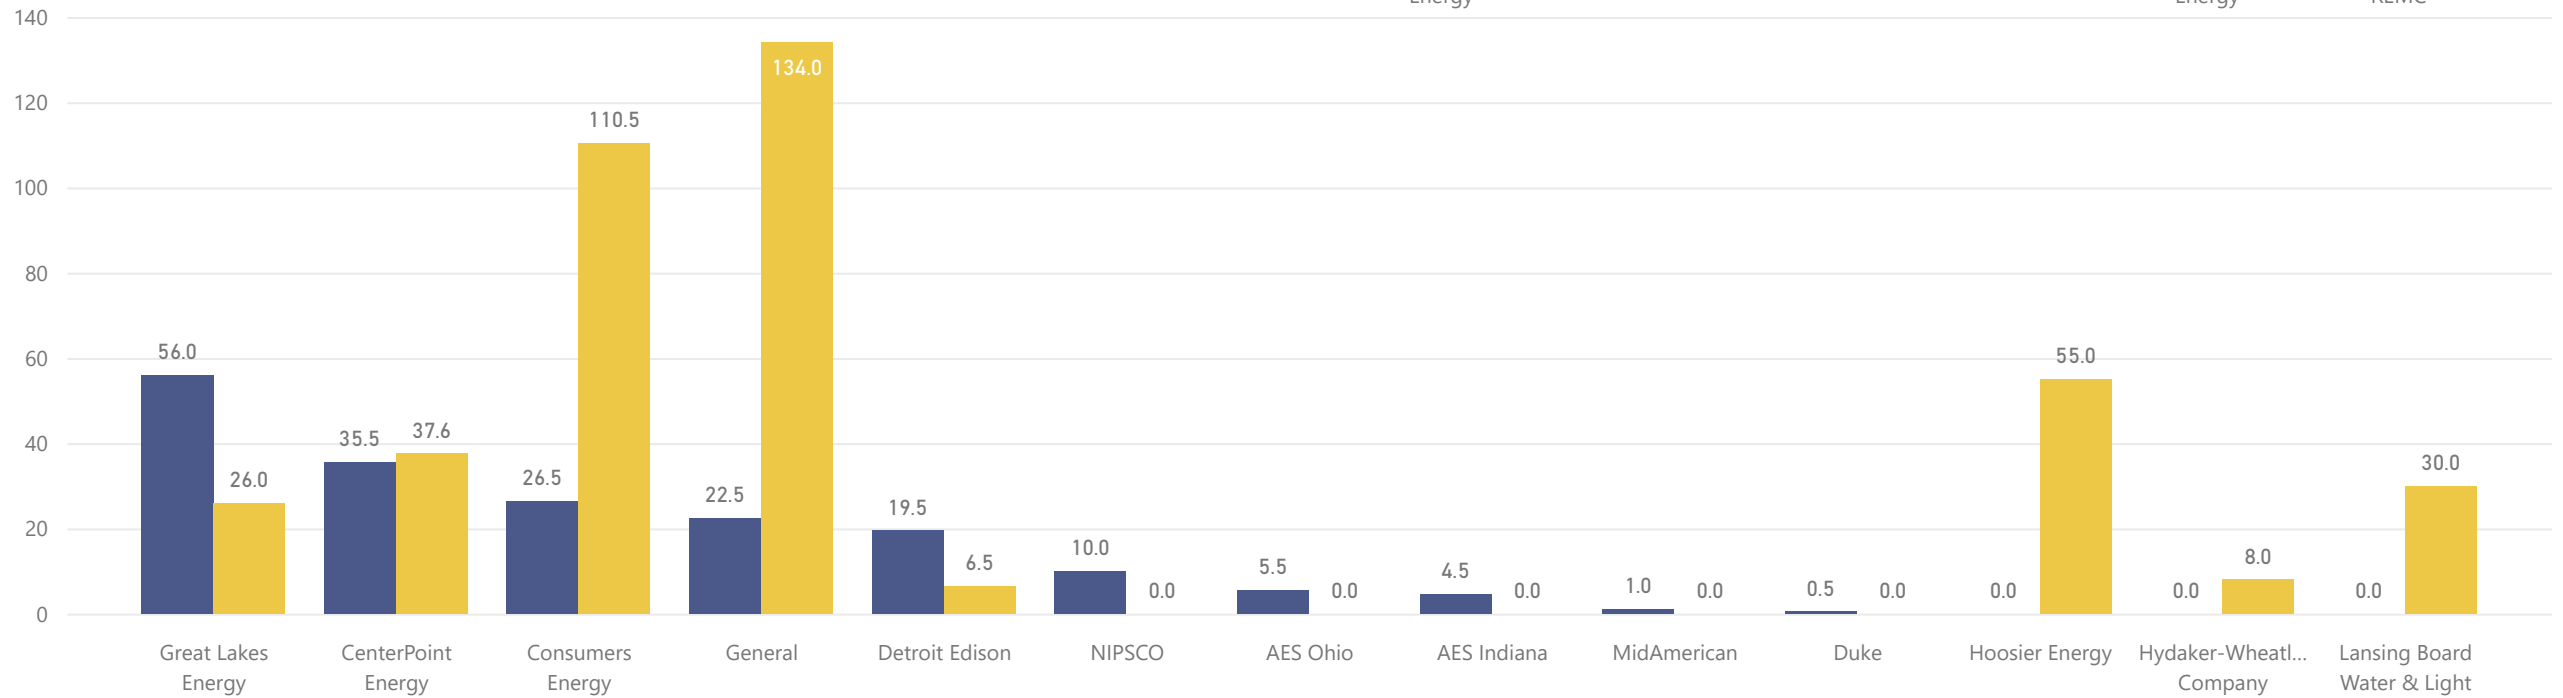


Billable Hours by Customer

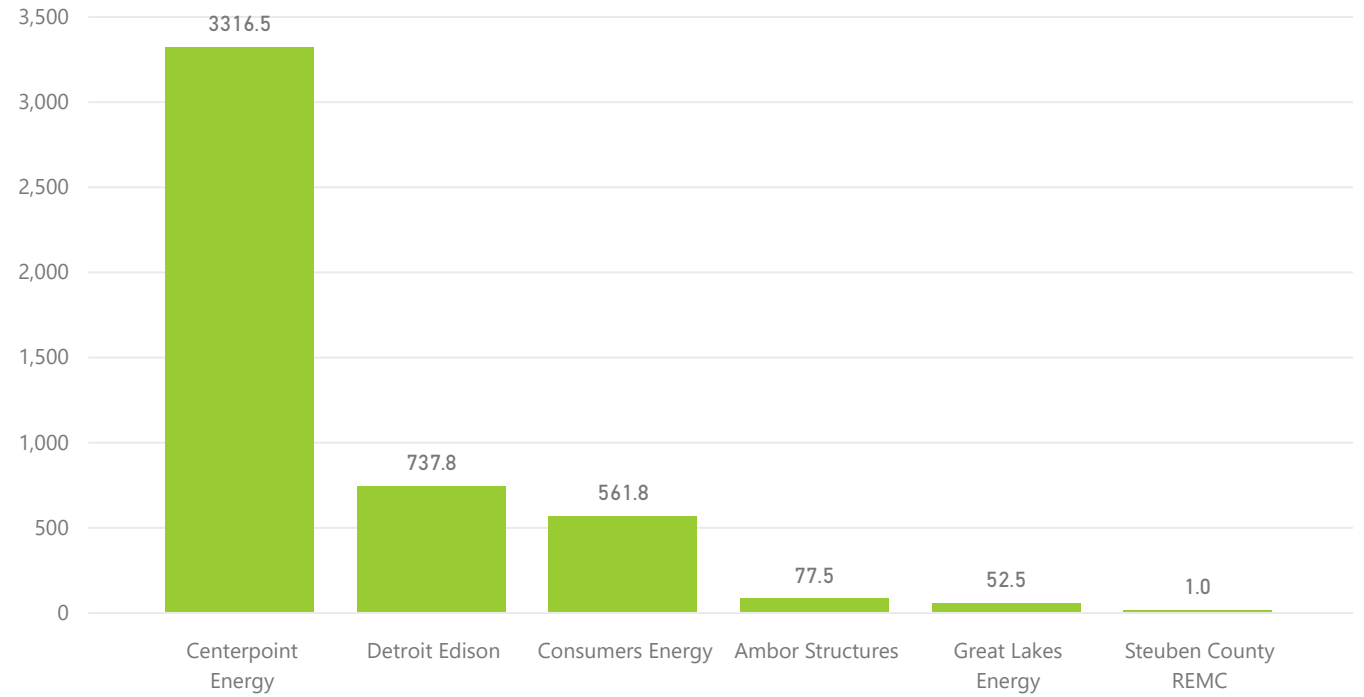


HWC EPC - Financials by Month

Net Profit

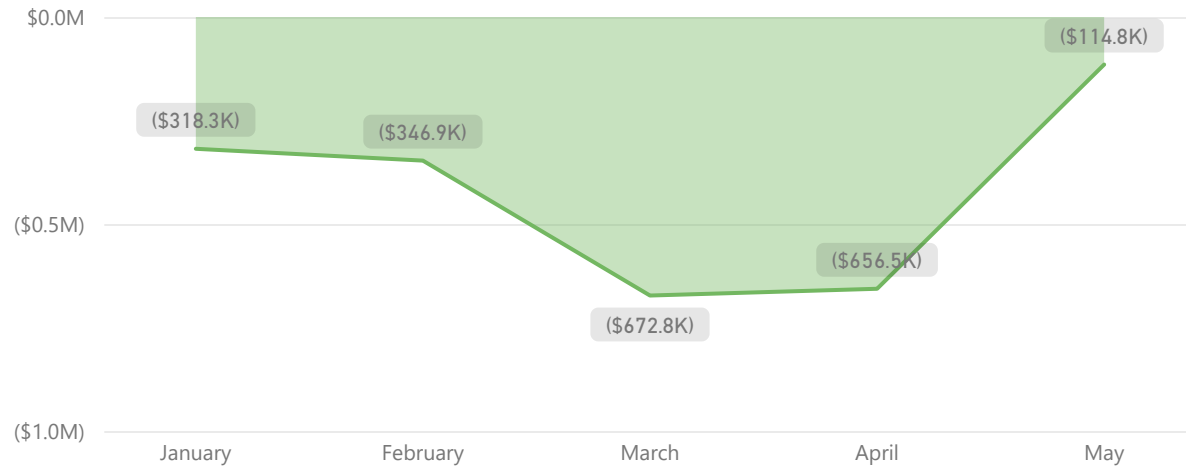


Revenue

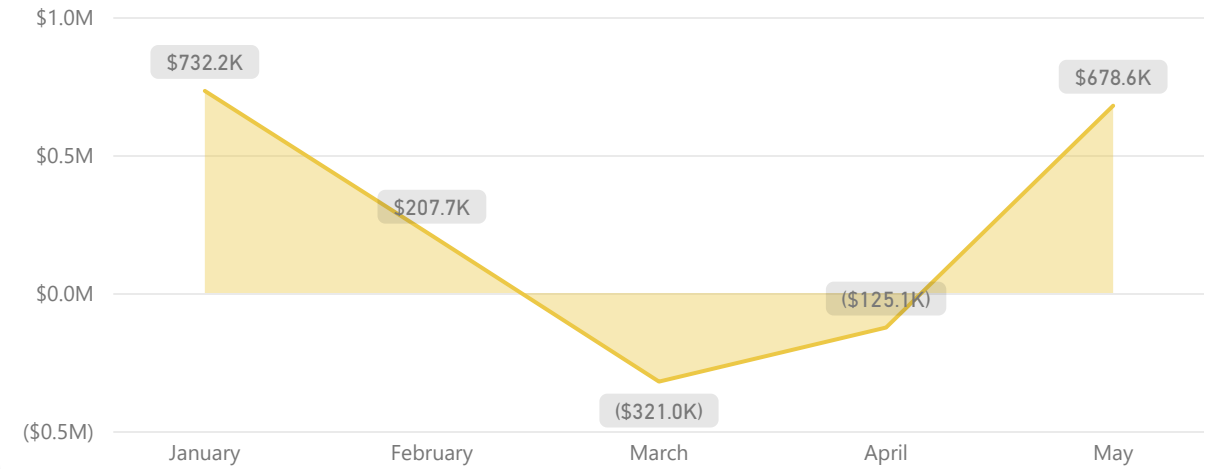


HWC EPC - Financials Year to Date




Net Profit

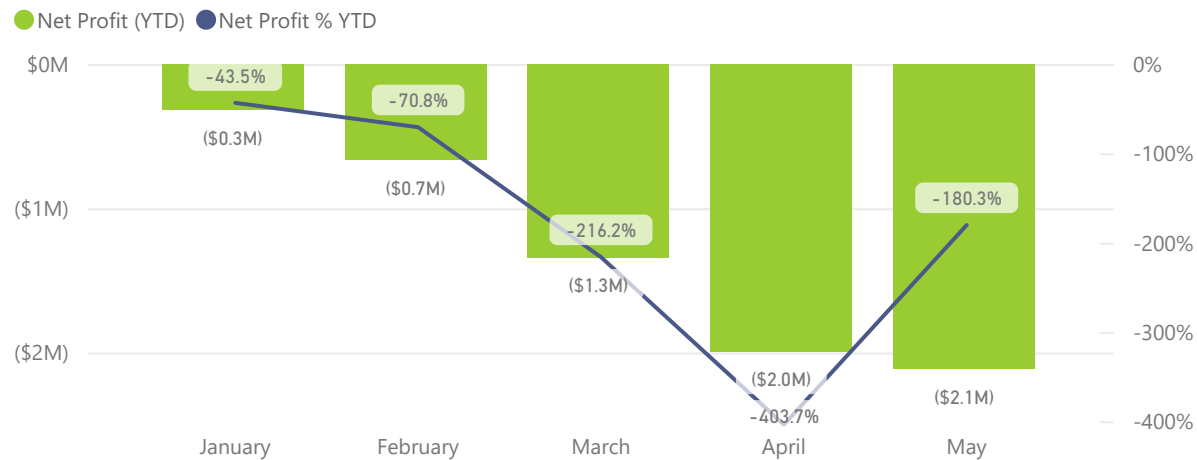

Revenue



CVR - Financials by Month

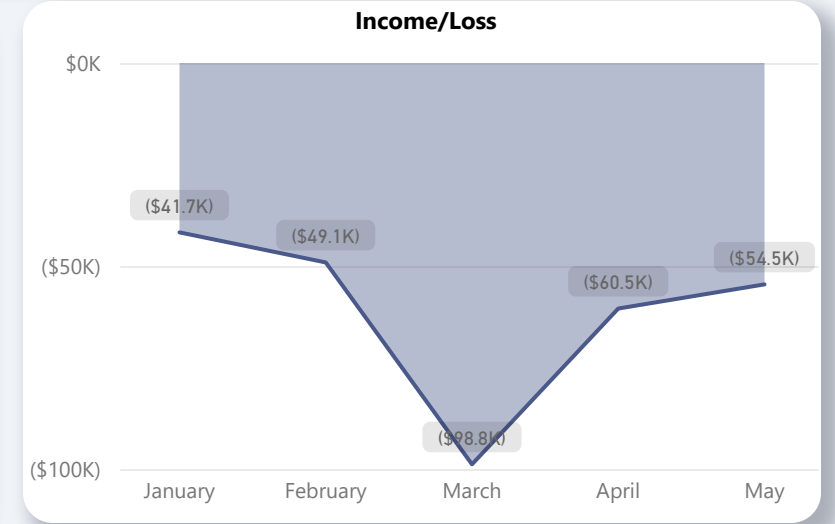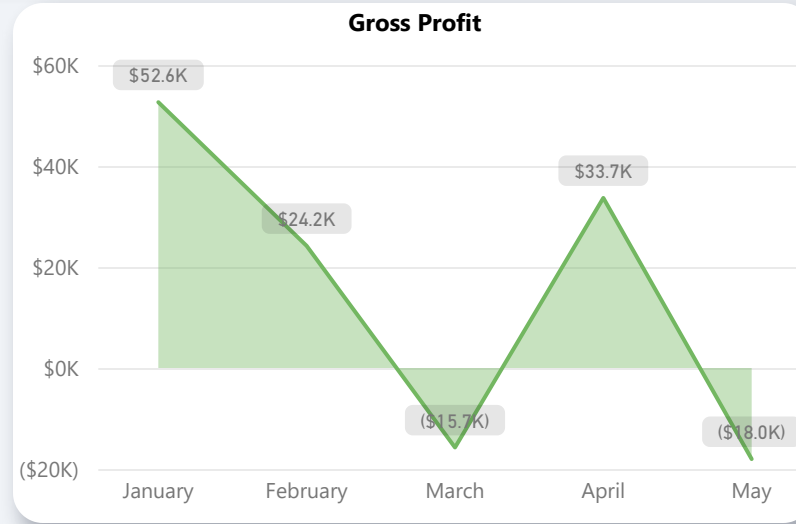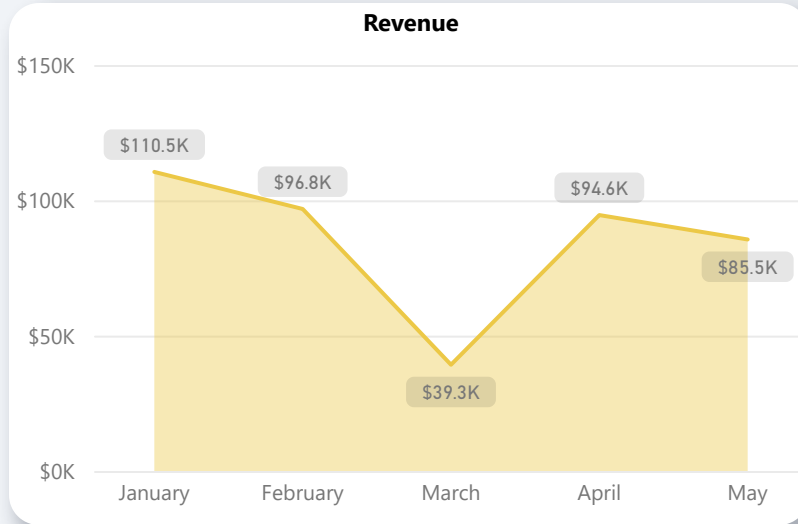

CVR - Financials Year to Date

